



Courthouse Project Update 01.23.20

WRITTEN UPDATE IN LIEU OF PHYSICAL MEETING

MONTHLY MEETING SERIES: next instance, 02.27.20

New and/or updated items indicated by bold italics

1. Schedule

a. ***Current Schedule Impacts***

- ***Ongoing:*** At this time, Hoffman and the Project Team are assessing any impacts from the weather events of 1/13-1/15.
- ***Resolved:*** Hoffman's previously reported schedule extension request, resulting from a series of requests for information regarding interior framing and window trim, has been resolved without adding days to the project schedule. Per contract, Hoffman is required to notify the County of any potential schedule impacts.
- Prior schedule impacts being monitored:
 - Hoffman's elevator subcontractor has been working since 11/14 to maintain a revised recovery schedule, due to delayed delivery and permitting.
 - Hoffman's exterior cladding subcontractor is on a recovery schedule due to delayed mobilization. The exterior cladding is a non-critical path item and should not impact substantial completion.

b. ***Upcoming Activities – see also 5.a-5.b. and 6.b.-6.d.***

Complete the Addition elevators; pour the remaining concrete walls, ramp, and planters for the new Courthouse entrance plaza; continue exterior site work on the North Campus; install the remainder of the Addition's building skin; perform early structural work above ceilings in the Commissioner Courts chambers area; install flooring and/or carpet tiles in the remainder of the Addition; complete comm, data, and fiber installation; commission the Addition's building systems.

c. ***Progress to Date***

Closed up the Addition stair tower after removing the man-lift (construction elevator); set carpet tile and rubber base on Addition Levels 2 through 5; set ceiling tiles on Addition Levels 2 through 5; replaced the cooling towers atop the Courthouse; built cab frames and set weights for both Addition elevator cars; poured the planter wall footings on the north and east sides of the Addition; framed and sheathed the Addition stair tower; installed cabinetry on Addition Levels 2 through 5; performed renovations in Courtrooms 2B through 2E and 5A through 5D.

2. Contract Metrics

- a. Hoffman given Notice To Proceed: 7/30/2018
- b. Phase 1 Projected Completion: 3/12/20
- c. ***Phase 2 Substantial Completion:*** 3/4/21
 - Reflects non-compensable time extensions to cover delays resulting from removal of contaminated soils and the remnants of the old County Detention Home, and from the February 2019 snowstorms.
- d. Original Project Budget (approved by Council 7/30/2018): \$76,579,770
 - Adjustment due to removal of art allowance: -\$441,417



- Revised Project Budget: \$76,138,353
- e. **Work Complete and Invoiced Through 11/30/19:** \$41,232,134

3. Changes

- None at this time.

4. Upcoming Project Decisions Needing Court Input

Due Date	Item

5. Stakeholder Concerns

- a. **Phase 2 Office Move Planning** – The Project Team held Phase 2 (2020-21) planning meetings with all building tenant groups and followed up with Hoffman Construction.
 - i. The County, OAC, and Hoffman are working together to finalize a Phase 2 logistics plan for distribution.
 - ii. Key objective is to keep as many courtrooms open and operating as possible.
 - iii. As of this morning (1/23), based on her one-on-one meetings with building user groups, Lynn has provided a final draft of the Phase 2 office moves plan.
 - iv. The Project Team will distribute the plan once it is fully vetted.
- b. **Jury Assembly Furniture** – Lynn Gray from Facilities has provided Superior Court with a plan for providing power and data to chairs so that jurors can plug in devices while waiting. The project architect, CBRE Heery, has provided Superior Court with a design for the room’s use as a ceremonial courtroom.
- c. **Minimizing Noise Disruptions** – The Project Team continues to provide advance notice to Superior and District Courts regarding activities which may carry major noise impacts, especially those which must continue in order to maintain schedule.

6. Announcements / Action Items

- a. **Hoffman Superintendent Transition** – Trent Dibble, Project Superintendent for Hoffman Construction, introduced his replacement, Mike Rotter. Trent is retiring in April.
- b. **Restroom Closure, Courthouse 2nd and 4th Floors** – Public restrooms on both floors are closed so that crews can make a connection between the Courthouse and Addition.
 - i. Signs posted will direct building users and visitors to other floors, or to the men’s room on the 2nd floor of the Mission Building.
 - ii. The men’s room on 2nd floor has been converted to a women’s room.
 - iii. Departmental restrooms on 4th floor will not be affected.
- c. **Current and Upcoming Courtroom and Chambers Work (2019-20)**
 - i. **3A (District Court Department 2)** – Ongoing since April 1. Millwork and casework are complete; audio-visual installation is near completion.
 - ii. **Commissioner Chambers Early Phase 2 Work (2019-20)** – Install above-ceiling structural steel elements in two Court IT offices on Level 1, then continue with selected Commissioner chambers.



- *The IT offices will become swing space for Commissioners displaced by structural steel and shear wall work before and during Phase 2.*
 - *Facilities will install a new temporary door to close off this hallway.*
- d. Next Meetings in Series – February 27, March 26, April 23.**

MEETING ATTENDANCE

	SUPERIOR COURT		COUNCIL		EXECUTIVE'S OFFICE
	Judge Bruce Weiss	X	Councilmember Sam Low		Ken Klein
X	Judge George Appel				Josh Dugan
X	Judge Linda Krese		SHERIFF'S OFFICE		
	Judge Millie Judge	X	Norm Link		DISTRICT COURT
	Commissioner Susan Gaer		Clint Korhonen		Judge Anthony Howard
X	Shane Nybo	X	Sean Gillespie		Judge Tam Bui
X	Andrew Somers			X	Marianne Boggie
			PROSECUTING ATTORNEY	X	Lonnie Enyeart
	CLERK'S OFFICE		Michael Held		
	Heidi Percy				OFFICE for PUBLIC DEFENSE
X	Mark Allen		LAW LIBRARY		Jason Schwarz
	Shelia Postle		Lettice Parker		Kristin Crane
	FACILITIES & FLEET		BAR ASSOCIATION		OAC SERVICES
X	Mark Thunberg	X	Joyce Wood	X	Kevin Fromm
X	Jeff Hencz	X	Cory Rein	X	Glen Lyons
X	Steve Slawson				Mary Ganz
X	Lolly Huggins		HOFFMAN CONSTRUCTION		
		X	Trent Dibble		
		X	Mike Rotter		

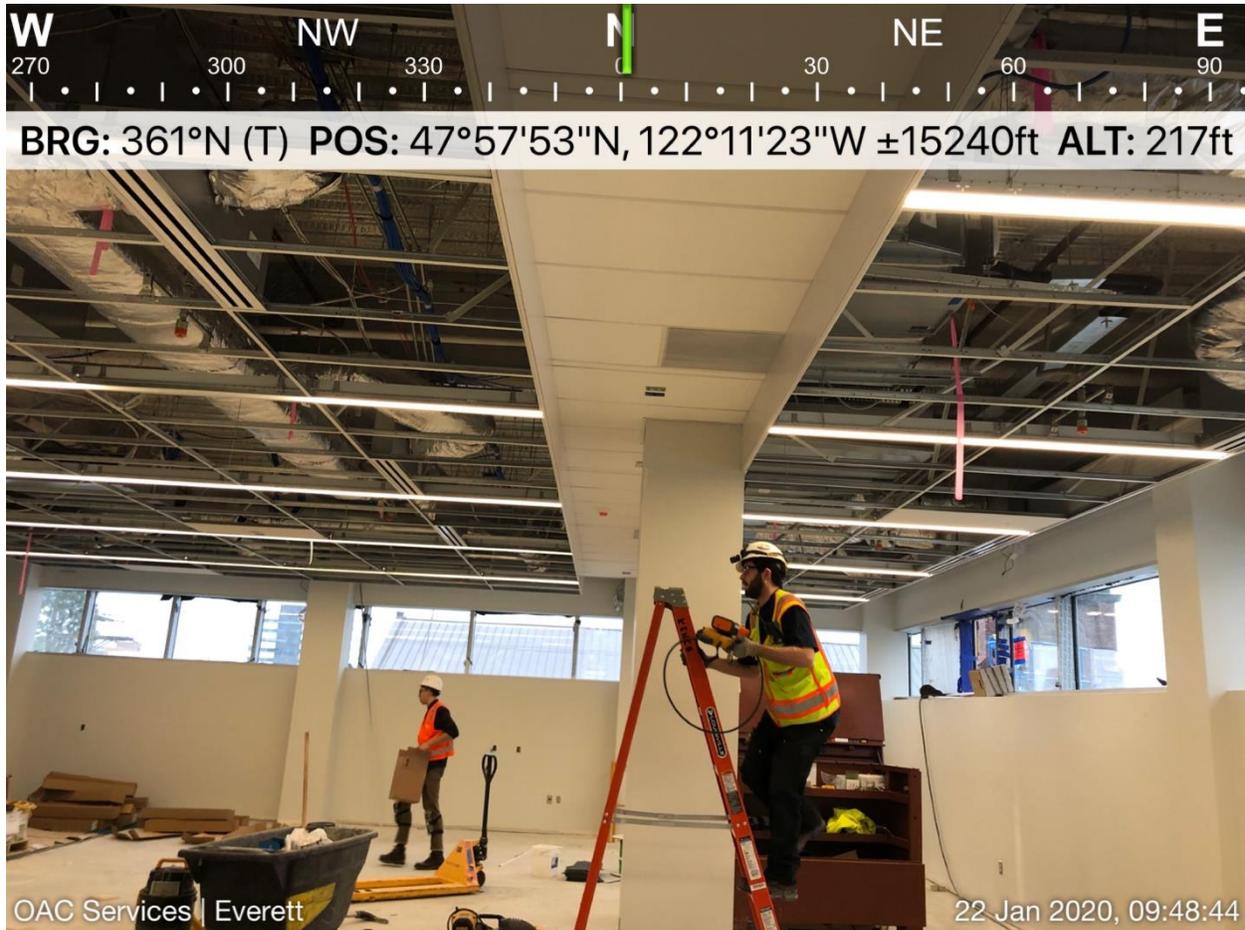


Figure 1: Courtroom Rosetta Stone

COURTROOM DESIGNATIONS BY FLOOR AND BY JUDGE			
NEW	CURRENT	JUDGE	NOTES
5A	Superior Dept 12	Ellis	
5B	Superior Dept 11	Krese	
5C	Superior Dept 9	Farris	
5D	Superior Dept 10	Weiss	
4A	NEW	TBD	<i>old Kinard Conference Room</i>
3A	District Dept 2	Bui	
3B	District Dept 3	Howard	
3C	District Dept 1	<i>(District Hearings)</i>	<i>to be relocated from 1 (east side)</i>
3D	N/A	<i>(shell space)</i>	
3E	Superior Dept 7	Wilson	
3F	Superior Dept 8	Lucas	
2A	C201	Thompson	<i>high-profile trial courtroom</i>
2B	Superior Dept 1	Alexander	<i>Judge Appel at DJJC</i>
2C	Superior Dept 2	Okrent	
2D	Superior Dept 3	Larsen	
2E	Superior Dept 4	Langbehn	<i>Judge Judge at DJJC</i>
1A	C304	<i>(Superior Court Criminal Hearings)</i>	<i>to be relocated from 3 (south side)</i>
NEW	CURRENT	COMMISSIONER	NOTES
1B	Commissioner A	Harness / Gaer	
1C	Commissioner B	Moriarty	
1D	Commissioner C	Harness / Gaer	
1E	Commissioner D	Waggoner	

The new courtroom numbering scheme represents the renovation's wayfinding improvements.

Figure 2: Progress Photo.



Overhead electrical work in the east half of the future Jury Assembly space.



Hoffman's most recent 6-week lookahead (01/21/20, first page)

ID	Activity Name	Sub	Dur	Start	Actual Start	Finish
Phase 1 - Addition, Existing Basement Remodel, RR Core				123	18-Sep-19 A	12-Mar-20
Phase 1 - New Addition				123	18-Sep-19 A	12-Mar-20
Phase 1 - New Addition - Building Envelope				111	18-Sep-19 A	25-Feb-20
C1653	Addition - Ext1 - Close-Up Building Envelope After Manlift Removal	MULTI		22	30-Dec-19 A	29-Jan-20
Phase 1 - New Addition - Building Envelope - West L2 to Roof				111	18-Sep-19 A	25-Feb-20
C2027	Addition - Ext - (L2 - Roof - West) - UHPC Panels	KCO		13	18-Sep-19 A	30-Jan-20
C2152	Addition - Ext1 - (All Elevations) - Vapor Barrier at Level 2 Canopy			7	30-Dec-19 A	21-Jan-20
C2043	Addition - Ext1 - (All Elevations) - Metal Panel Lead time #1	KCO		13	08-Jan-20 A	24-Jan-20
C2178	Addition - Ext1 - (All Elevations) - Metal Panel Lead time #2	KCO		14	10-Jan-20 A	29-Jan-20
C2028	Addition - Ext1 - (All Elevations) - Composite Metal Panels #1	KCO		10	27-Jan-20	07-Feb-20
C2180	Addition - Ext1 - (All Elevations) - Metal Panel Field Measure Vestibule	KCO		1	29-Jan-20*	29-Jan-20
C2179	Addition - Ext1 - (All Elevations) - Composite Metal Panels #2	KCO		10	30-Jan-20	12-Feb-20
C2181	Addition - Ext1 - (All Elevations) - Metal Panel Lead time Vestibule	KCO		14	30-Jan-20	18-Feb-20
C2182	Addition - Ext1 - (All Elevations) - Composite Metal Panels Vestibule	KCO		5	19-Feb-20	25-Feb-20
Phase 1 - New Addition - Building Envelope - North L2 to Roof				17	29-Oct-19 A	23-Jan-20
C2029	Addition - Ext (L2 - Roof - North) - UHPC Panels	KCO		17	29-Oct-19 A	23-Jan-20
Phase 1 - New Addition - Interior Buildout & Fit-Up				67	09-Dec-19 A	12-Mar-20
Phase 1 - New Addition - Interior Buildout & Fit-Up - Level 1				34	02-Jan-20 A	18-Feb-20
C1492	Addition L1 - Install Flooring & Base	D9		15	02-Jan-20 A	05-Feb-20
C1489	Addition L1 - Trim Out Mechanical	HP		3	29-Jan-20*	31-Jan-20
C1490	Addition L1 - Trim Out Electrical	VECA		3	29-Jan-20*	31-Jan-20
C1491	Addition L1 - Trim Out Fire Sprinklers	HP		3	29-Jan-20*	31-Jan-20
C1495	Addition L1 - Install Furniture & Appliances			2	30-Jan-20*	31-Jan-20
C1494	Addition L1 - Install Casework / Millwork / Interior Storefront	ART		5	30-Jan-20	05-Feb-20
C1485	Addition L1 - Install ACT	AP		5	03-Feb-20*	07-Feb-20
C1496	Addition L1 - Clean & Pre-Punchlist			3	07-Feb-20	11-Feb-20
C1493	Addition L1 - Construction Complete	HCC		0		07-Feb-20
C1497	Addition L1 - Pre-Punchlist Corrections	HCC		5	12-Feb-20	18-Feb-20
Phase 1 - New Addition - Interior Buildout & Fit-Up - Level 2				9	22-Jan-20	03-Feb-20
C1518	Addition L2 - Construction Complete	HCC		0		24-Jan-20
C1521	Addition L2 - Clean & Pre-Punchlist			1	28-Jan-20	28-Jan-20
C1522	Addition L2 - Pre-Punchlist Corrections	HCC		5	28-Jan-20	03-Feb-20
Level 2 - Areas Affected by RFIs 0373 Rev 3 / 0429 Rev 2 / 0438				5	22-Jan-20	28-Jan-20
C2115	Addition L2 - Install Flooring & Base	D9		3	22-Jan-20*	24-Jan-20
C2113	Addition L2 - ACT Tiles	AP		2	27-Jan-20	28-Jan-20
Phase 1 - New Addition - Interior Buildout & Fit-Up - Elevators				41	16-Jan-20 A	12-Mar-20
C2098	Addition Elevator - Terminate Controller	KONE		5	16-Jan-20 A	22-Jan-20
C2145	Addition Elevator - Interior	KONE		2	20-Jan-20 A	21-Jan-20
C2099	Addition Elevator - Adjust / Commission	KONE		12	22-Jan-20	06-Feb-20
C2100	Addition Elevator - Pre Testing - Fire Life Safety	KONE		3	07-Feb-20	11-Feb-20
C2101	Addition Elevator - Final Inspections - 2 Elevators	KONE		2	12-Feb-20	13-Feb-20
C1096	Addition Elevator - Final Clean & Punchlist	HCC		10	14-Feb-20	27-Feb-20
C1643	Addition Elevator - Punchlist Corrections	HCC		10	28-Feb-20	12-Mar-20
Phase 1 - New Addition - Interior Buildout & Fit-Up - Stairs				41	09-Dec-19 A	05-Feb-20
C2080	Addition Stairs - UHPC Panels at Stair 1	KCO		15	09-Dec-19 A	30-Jan-20
C2077	Addition Stairs - Complete Framing / Interior Sheathing / GWB / Tape at S	AP		14	10-Dec-19 A	24-Jan-20
C2079	Addition Stairs - Painting GWB at Stair 1	NWC		5	27-Jan-20	31-Jan-20
C2078	Addition Stairs - Painting Stair 1 Steel	NWC		8	27-Jan-20	05-Feb-20



Hoffman's most recent 6-week lookahead (01/21/20, continued)

ID	Activity Name	Sub	Dur	Start	Actual Start	Finish
Phase 1 - New Addition - Site Finishes				64	25-Nov-19 A	26-Feb-20
C2036	Site - Walls / Planters / Stairs / Upper Slab / ADA Ramp East of 12.1 Line	MM		42	25-Nov-19 A	27-Jan-20
C2176	Site - Steel / Framing / Sheathing / Weatherproofing at Vestibule	MULTI		9	13-Jan-20 A	23-Jan-20
C2229	Site - Establish Grade for Stairs / Lower Plaza and Planters ***Extreme W	IW		3	20-Jan-20 A	22-Jan-20
C2236	Site - FRP Footing at Wall 8	MM		3	20-Jan-20 A	22-Jan-20
C2172	Site - FRP Stairs ***Extreme Weather Week of 1/13/20	MM		9	22-Jan-20	03-Feb-20
C2237	Site - FRP Wall 8	MM		3	23-Jan-20	27-Jan-20
C2228	Site - Pour Decorative Bands ***Extreme Weather Week of 1/13/20	MM		2	27-Jan-20*	28-Jan-20
C2175	Site - Pour Lower Plaza	MM		1	29-Jan-20	29-Jan-20
C2037	Site - Landscape / Irrigation / Soil Installation East of 12.1 Line	A-1		5	03-Feb-20*	07-Feb-20
C2232	Site - Pour Stair Landings	MM		1	04-Feb-20	04-Feb-20
C2221	Site - Grading for ADA Ramps and Curbs	MM		2	05-Feb-20	06-Feb-20
C2222	Site - FRP ADA Ramps and Curbs	MM		6	07-Feb-20	14-Feb-20
C2234	Site - FRP Fire Lane	MM		8	17-Feb-20	26-Feb-20
Phase 1 - New Addition - Commissioning & Startup				44	06-Jan-20 A	05-Mar-20
C2183	Addition Cx - Lighting Control Programming	VECA		5	06-Jan-20 A	21-Feb-20
C1743	Addition - Installation & Testing of Security System (by Owner)	Owner		10	13-Jan-20 A	24-Jan-20
C2190	Addition Cx - Power to DOAS	VECA		2	13-Jan-20 A	24-Jan-20
C1649	Addition - Final Inspections / Test & Commission	HCC		30	17-Jan-20 A	27-Feb-20
C2185	Addition Cx - Lighting Integration Graphics	JCI		5	20-Jan-20 A	24-Jan-20
C2188	Addition Cx - EF PGM / Point to Point	JCI		1	24-Jan-20*	24-Jan-20
C2192	Addition Cx - System Readiness Checklist	VECA		1	24-Jan-20*	24-Jan-20
C2194	Addition Cx - FPTs - Safety / Security	KBA		1	27-Jan-20	27-Jan-20
C2200	Addition Cx - Fire Pump Testing	RHFP		1	27-Jan-20*	27-Jan-20
C2196	Addition Cx - VRF Front End Graphics	JCI		4	27-Jan-20	30-Jan-20
C2193	Addition Cx - Daikan VRF / DOAS Start Up	HP		5	27-Jan-20	31-Jan-20
C2191	Addition Cx - DOAS PGM / Point to Point	JCI		1	28-Jan-20*	28-Jan-20
C2198	Addition Cx - FPTs Plumbing	KBA		1	30-Jan-20	30-Jan-20
C2197	Addition Cx - TAB (Air Test)	HP		20	30-Jan-20*	26-Feb-20
C2201	Addition Cx - System Readiness FAATS	VECA		1	31-Jan-20*	31-Jan-20
C2202	Addition Cx - Audio Visual	VECA		2	31-Jan-20	03-Feb-20
C2203	Addition Cx - Fire Systems Final	RHFP		1	03-Feb-20*	03-Feb-20
C2199	Addition Cx - FPTs HVAC	KBA		20	04-Feb-20*	02-Mar-20
C2211	Addition Cx - Metering	VECA		1	12-Feb-20*	12-Feb-20
C2212	Addition Cx - Meter Integration	JCI		2	13-Feb-20	14-Feb-20
C2225	Addition - Interior Clean for Owner Punchlist	HCC		3	14-Feb-20	18-Feb-20
C2213	Addition Cx - FPTs Metering	KBA		1	17-Feb-20*	17-Feb-20
C2223	Addition - Phase 1 - Owner and A / E Interior Punchlist	Owner		3	18-Feb-20*	20-Feb-20
C2195	Addition Cx - Lighting Control - Basement Level	VECA		1	21-Feb-20	21-Feb-20
C2204	Addition Cx - Lighting Control - Level 1	VECA		1	21-Feb-20	21-Feb-20
C2205	Addition Cx - Lighting Control - Level 2	VECA		1	21-Feb-20	21-Feb-20
C2206	Addition Cx - Lighting Control - Level 3	VECA		1	21-Feb-20	21-Feb-20
C2207	Addition Cx - Lighting Control - Level 4	VECA		1	21-Feb-20	21-Feb-20
C2208	Addition Cx - Lighting Control - Level 5	VECA		1	21-Feb-20	21-Feb-20
C2210	Addition Cx - Fire Alarm Factory Start Up	VECA		5	21-Feb-20	27-Feb-20
C1651	Addition - Phase 1 - Owner and A / E Punchlist Corrections	HCC		10	21-Feb-20	05-Mar-20



Hoffman's most recent 6-week lookahead (01/21/20, continued)

ID	Activity Name	Sub	Dur	Start	Actual Start	Finish
C2226	Addition - Exterior Clean for Owner Punchlist	HCC	3	26-Feb-20	28-Feb-20	
C2214	Addition Cx - TAB Backcheck	KBA	2	27-Feb-20	28-Feb-20	
C2217	Addition Cx - FPTs Fire Suppression / Alarm	KBA	1	02-Mar-20	02-Mar-20	
C2220	Addition Cx - Owner Training - HVAC / Plumbing	HP	1	02-Mar-20*	02-Mar-20	
C2224	Addition - Phase 1 - Owner and A / E Exterior Punchlist	Owner	1	02-Mar-20*	02-Mar-20	
C2219	Addition Cx - Owner Training - BAS	JCI	2	02-Mar-20*	03-Mar-20	
C2215	Addition Cx - Fire Marshall Inspection	VECA	1	03-Mar-20	03-Mar-20	
C2216	Addition Cx - Fire Marshall DAS	VECA	1	03-Mar-20	03-Mar-20	
Phase 1 - New Restroom Core in Existing Building				20	07-Feb-20	05-Mar-20
Phase 1 - New Restroom Core - Commissioning & Startup				20	07-Feb-20	05-Mar-20
C1640	New RR Core - Final Inspections / Test & Commission	HCC	15	07-Feb-20	27-Feb-20	
C1641	New RR Core - Final Clean & Punchlist		5	28-Feb-20	05-Mar-20	
Phase 2 - Existing Courthouse Renovation				161	17-Jun-19 A	04-Feb-20
Phase 2 - South Shearwall				5	17-Jun-19 A	03-Feb-20
C1984	SSW - FRP Shearwall Footing	IW	5	17-Jun-19 A	03-Feb-20	
Phase 2 - Level 2 Renovation				2	30-Dec-19 A	28-Jan-20
Phase 2 - Level 2 Renovation - Early Work South of F Line				2	30-Dec-19 A	28-Jan-20
C2151	Existing L2 - Ceiling Tile at ACT Grid	AP	2	30-Dec-19 A	28-Jan-20	
Phase 2 - Trial Courtroom Renovations				7	27-Jan-20	04-Feb-20
Phase 2 - Courtroom 3A				7	27-Jan-20	04-Feb-20
C2155	Courtroom 3A - Install Audio Visual Equipment		5	27-Jan-20*	31-Jan-20	
C1704	Courtroom 3A - Final Clean & Punchlist	HCC	1	03-Feb-20	03-Feb-20	
C1705	Courtroom 3A - Punchlist Corrections	HCC	1	04-Feb-20	04-Feb-20	
C1706	Courtroom 3A - TCO	HCC	0		04-Feb-20	
