



Courthouse Project Update 09.25.20

WRITTEN UPDATE IN LIEU OF PHYSICAL MEETING

MONTHLY MEETING SERIES: next scheduled instance, 10.22.2020

New and/or updated items indicated by bold italics

3000 Rockefeller Ave., M/S 404
Everett, WA 98201-4046
425.388.3087
www.snoco.org

Dave Somers
County Executive

1. Schedule

a. Schedule

- **Current Status:**

- **COVID-19 EFFECTS:** On July 10th, Hoffman Construction filed a claim in response to denial of their proposed change order, submitted May 13, requesting compensable time related to pandemic effects. Snohomish County has denied the claim.
- The County notified Hoffman and Performance Abatement, via letters dated April 7, May 26, June 23, and September 1, 2020, that the pandemic constitutes a force majeure event. The County did not request or require Hoffman and Performance Abatement to continue work; both firms have continued work. Schedule time extensions, but not costs, are allowed under force majeure. The Project Team and Hoffman Construction are reaching consensus on compensable COVID-related compliance costs.
- Due to ongoing pandemic-related challenges regarding labor availability and supply chain impacts, building user groups will remain in temporary offices longer than originally scheduled.
- The exact length of any schedule delays is still being calculated and is based on pandemic-related impacts.
- Both Hoffman and Performance are fulfilling their contractual obligations to report potential cost and schedule impacts, and both continue to follow state guidelines in performing their work.

b. **Upcoming Activities – see also 5.a-5.b. and 6.a.-6.e.**

Complete and turn over Courtroom 1A; continue demolition and abatement on Level 4; complete demolition and abatement in the vacated Level 4 and 5 restrooms; complete floor tile installation on the east side of Level 1; install ceiling tiles over the Office for Public Defense, Courtroom 1A, and public corridors; complete MEP (mechanical, electrical, and plumbing) reroutes above ceilings in Courtroom 2A; continue overhead MEP (mechanical, electrical, and plumbing) and fire sprinkler installation on Level 2; continue transforming the vacated Level 2 restrooms into a family restroom, janitor's closet, and lactation room; continue irrigation and landscaping northwest of the Courthouse; form and pour the south shear wall in the tunnel; continue renovating the existing Courthouse elevators; complete punchlist corrections in and around the Addition.



c. Progress to Date

Began irrigation, site utilities, and re-grading northwest of the Courthouse; installed doors and hardware around a new secure elevator stop at Level 1; performed additional wall demolition in Court Commissioner chambers and Confirmations ahead of shear wall construction; completed demolition and abatement on Level 2 around the main corridor, above ceilings in Courtroom 2A, and in the mechanical penthouse; installed carpeting in the Court Commissioner hallway and in select offices and rooms on Level 1; installed the ceiling grid, lighting, and data cabling around Courtroom 1A; removed the concrete retaining wall around Wall Street at Wetmore Avenue; completed drywall and overhead and in-wall electrical work on the east side of Level 1; completed abatement, demolition, seismic collector plates, electrical, lighting, and drywall in the Office for Public Defense; created the new vestibule for the Office for Public Defense; completed above-ceiling demolition on the southwest side of the Courthouse's Level 2; completed demolition of the vacated Level 2 restrooms; poured the south shear wall footing.

2. Contract Metrics

- a. Hoffman given Notice To Proceed: 7/30/2018
- b. Phase 1 Completion: 3/12/20
- c. Phase 2 Substantial Completion: Estimated to shift to approximately 6/14/21 due to COVID-related schedule adjustments.
 - Subject to change due to pandemic-related schedule impacts. These are still being measured by Hoffman Construction and Performance Abatement and will then be reviewed and assessed by the Project Team.
 - The current substantial completion date reflects non-compensable time extensions resulting from removal of contaminated soils and the remnants of the old County Detention Home, and from the February 2019 snowstorms.
- d. Original Project Budget (approved by Council 7/30/2018): \$76,579,770
 - Adjustment due to removal of art allowance: -\$441,417
 - Revised Project Budget: \$76,138,353
- e. **Work Complete and Invoiced Through 7/31/20: \$56,133,853**

3. Changes

- None at this time.

4. Upcoming Project Decisions Needing Court Input

Due Date	Item



5. Stakeholder Concerns

- a. **Phase 2 Office Move Plan** – *The general Phase 2 office moves plan has been distributed by Facilities and Fleet Management. Lynn Gray from Facilities is working with each building user group on moving specific offices and individuals at specific times, once their destination spaces are ready. COVID-19 has impacted this schedule and user groups will be delayed moving to destination spaces.*
- b. **Minimizing Noise Disruptions** – *The Project Team continues to provide advance notice to Superior and District Courts regarding activities which may carry major noise impacts, especially those which must continue in order to maintain schedule.*

6. Announcements / Action Items

- a. **Courtrooms 3E and 3F** – *Renovations in these courtrooms will begin in mid-October and continue through January. Crews will work on one courtroom and one jury room at a time.*
 - b. **Meetings Going Forward** – *Our next three scheduled meetings are October 22, November 19, and December 17. Per the current public health emergency, we will advise of any alternate meeting / teleconferencing arrangements, or of any cancellations or postponements.*
-

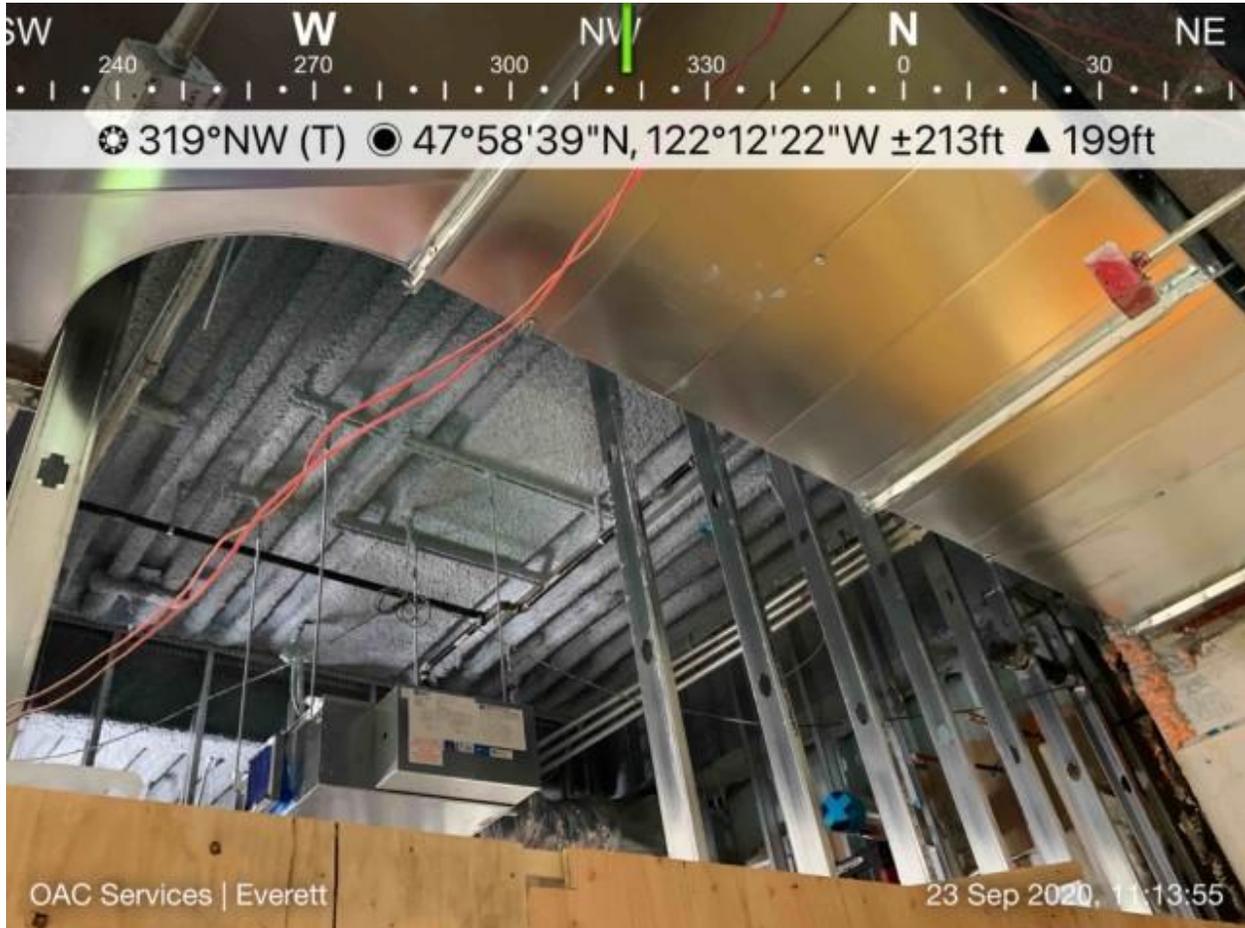


Figure 1: Courtroom Rosetta Stone: Courtroom Assignments – Effective 8/13/20

COURTROOM DESIGNATIONS BY FLOOR AND BY JUDGE			
NEW	CURRENT	JUDGE	NOTES
5A	Superior Dept 12	Ellis	
5B	Superior Dept 11	Dingledy	
5C	Superior Dept 9	Farris	
5D	Superior Dept 10	Weiss	
4A	NEW	TBD	<i>old Kinard Conference Room</i>
3A	District Dept 2	Bui	
3B	District Dept 3	Howard	
3C	District Dept 1	<i>(District Hearings)</i>	<i>to be relocated from 1 (east side) in early 2021; temporarily relocating to Basement in 2020</i>
3D	N/A	<i>(shell space)</i>	
3E	Superior Dept 7	Okoloko	
3F	Superior Dept 8	Lucas	
2A	C201	Alexander	<i>high-profile trial courtroom</i>
2B	Superior Dept 1	Appel	
2C	Superior Dept 2	Okrent	
2D	Superior Dept 3	Thompson	
2E	Superior Dept 4	Langbehn	
1A	C304	<i>(Superior Court Criminal Hearings)</i>	<i>to be relocated from 3 (south side) in late 2020</i>
2F	<i>Assigned to Dept. 5 Mission Building</i>	Judge	
2G	<i>Assigned to Dept. 6 Mission Building</i>	Kurtz	
--	<i>Assigned to DJJC</i>	<i>Wilson</i>	<i>At DJJC until MM/DD/YYYY - TBD</i>
--	<i>Assigned to DJJC</i>	<i>Larsen</i>	<i>At DJJC until MM/DD/YYYY - TBD</i>
NEW	CURRENT	COMMISSIONER	NOTES
1B	Commissioner A	Harness	
1C	Commissioner B	Nelson	
1D	Commissioner C	Brudvik	
1E	Commissioner D	Moriarty	

The new courtroom numbering scheme represents the renovation's wayfinding improvements and reflects upcoming courtroom assignments.

Figure 2: Progress Photo



Framing, electrical and plumbing rough-in, and ductwork installation above the future second-floor janitor's closet (former men's room).



Hoffman's most recent 6-week lookahead (09/22/20, first page)

ID	Activity Name	Sub	Dur	Start	Finish
Snohomish County Courthouse (Current)			194	24-Feb-20 A	24-Nov-20
Staff Relocation Notifications			10	09-Oct-20	23-Oct-20
SVT15	Notification - 74 Days Prior to Existing Building Level 4 Work	HCC	0		09-Oct-20
SVT14	Notification - 74 Days Prior to Existing Building Level 3 Work	HCC	0		16-Oct-20
SVT16	Notification - 74 Days Prior to Existing Building Level 5 Work	HCC	0		23-Oct-20
COVID-19			163	13-Mar-20 A	30-Oct-20
SVT36	COVID-19 - Global Pandemic Restrictions	MULTI	163	13-Mar-20 A	30-Oct-20
Phase 1 - Addition, Existing Basement Remodel, RR Core			61	03-Aug-20 A	27-Oct-20
Phase 1 - New Addition			61	03-Aug-20 A	27-Oct-20
Phase 1 - New Addition - Site Finishes			60	03-Aug-20 A	26-Oct-20
C2039	Site - Sitework / Landscaping West of 12.1 Line	A-1	60	03-Aug-20 A	26-Oct-20
Phase 1 - New Addition - Commissioning & Startup			1	27-Oct-20	27-Oct-20
C2209	Addition Cx - FPTs Irrigation	KBA	1	27-Oct-20	27-Oct-20
Phase 2 - Existing Courthouse Renovation			194	24-Feb-20 A	24-Nov-20
Phase 2 - South Shearwall			17	13-Oct-20	04-Nov-20
Phase 2 - Basement Shearwall			17	13-Oct-20	04-Nov-20
C2435	SSW BL - Demo SOMD for Rebar at Level 1	PAS	2	13-Oct-20	14-Oct-20
C2433	SSW BL - Form Basement to Level 1	IW	7	15-Oct-20	23-Oct-20
C2434	SSW BL - Rebar Basement to Level 1	IW	8	26-Oct-20	04-Nov-20
Phase 2 - Level 1 Renovation			42	10-Sep-20 A	06-Nov-20
C1261	Existing L1 - Final Inspections / Test & Commission	HCC	20	09-Oct-20	05-Nov-20
C1234	Existing L1 - Install Furniture & Appliances	Owner	2	19-Oct-20*	20-Oct-20
Phase 2 - Level 1 Renovation - GL C-F / 16-24 - PRIORITY 1A (A)			15	21-Sep-20 A	09-Oct-20
C2350	Existing L1 A - Set Plumbing Fixtures (includes Family Restroom 1019)	HP	4	21-Sep-20 A	24-Sep-20
C2292	Existing L1 A - Millwork Courtroom GL C-E	ART	15	21-Sep-20 A	09-Oct-20
C2288	Existing L1 A - Plumbing Trim Out	HP	3	25-Sep-20	29-Sep-20
C2354	Existing L1 A - Install Doors & Hardware	BHW	3	28-Sep-20*	30-Sep-20
C2293	Existing L1 A - Install ACT Tiles	AP	4	02-Oct-20*	07-Oct-20
Phase 2 - Level 1 Renovation - Office of Public Defense Rooms 1500 / 1510 / 1515 / 1520 (B)			7	23-Sep-20	01-Oct-20
C2345	Existing L1 B - Elec Trim Out	VECA	1	23-Sep-20*	23-Sep-20
C2263	Existing L1 B - Patch Spline Ceiling	AP	4	23-Sep-20*	28-Sep-20
C2268	Existing L1 B - Millwork	ART	2	24-Sep-20*	25-Sep-20
C2344	Existing L1 B - Doors & Hardware	BHW	1	28-Sep-20*	28-Sep-20
C2365	Existing L1 B - Install Vinyl Tile 1500 / 1520	D9	2	28-Sep-20	29-Sep-20
C2367	Existing L1 B - Install Base 1500 / 1520 / 1520	D9	2	28-Sep-20	29-Sep-20
C2269	Existing L1 B - Install ACT Grid 1500	AP	1	30-Sep-20*	30-Sep-20
C2270	Existing L1 B - Install ACT Tiles 1500	AP	1	01-Oct-20	01-Oct-20
Phase 2 - Level 1 Renovation - Public Lobby Rooms 1050 / 1100 / 1300 - PRIORITY 1A (C)			17	10-Sep-20 A	02-Oct-20
C2290	Existing L1 C - Install Large Format Floor Tile & Grout	D9	5	10-Sep-20 A	24-Sep-20
C2381	Existing L1 C - Install ACT Tiles	AP	3	28-Sep-20*	30-Sep-20
C2427	Existing L1 C - Install Rubber Base	D9	2	01-Oct-20	02-Oct-20
C2460	Existing L1 C - Install Carpet in Waiting Room 1300	D9	2	01-Oct-20	02-Oct-20
Phase 2 - Level 1 Renovation - Shearwall / Collector Plates GL C / 5-15 (D)			10	26-Oct-20	06-Nov-20
C2437	Existing L1 D - Form	IW	5	26-Oct-20	30-Oct-20



Hoffman's most recent 6-week lookahead (09/22/20, continued)

ID	Activity Name	Sub	Dur	Start	Finish
C2438	Existing L1 D - Rebar	IW	5	02-Nov-20	06-Nov-20
Phase 2 - Level 1 Renovation - Early Turnover Area (G)			20	08-Oct-20	04-Nov-20
C2540	Existing L1 G - Hoffman Punchlist Walk	HCC	1	08-Oct-20	08-Oct-20
C2541	Existing L1 G - Hoffman Punchlist Corrections	HCC	6	09-Oct-20	16-Oct-20
C2542	Existing L1 G - FPT for Plumbing (Including Inmate Holding Plumbing Fixt	HP	2	15-Oct-20	16-Oct-20
C2543	Existing L1 G - Lighting Integration Graphics	JCI	3	15-Oct-20	19-Oct-20
C2544	Existing L1 G - Fire Alarm System Readiness	HCC	3	15-Oct-20	19-Oct-20
C2545	Existing L1 G - Point to Point for VAV & Exhaust Fans	HCC	5	15-Oct-20	21-Oct-20
C2550	Existing L1 G - TAB (Air Test)	KBA	7	20-Oct-20	28-Oct-20
C2546	Existing L1 G - Preliminary Sitewalk with City Inspector	KBA	1	22-Oct-20	22-Oct-20
C2548	Existing L1 G - FPT for Lighting	HP	2	22-Oct-20	23-Oct-20
C2549	Existing L1 G - Installation & Testing of Security System (Including Inmate	SMNS	5	22-Oct-20	28-Oct-20
C2547	Existing L1 G - Preliminary Sitewalk with Fire Marshal	SMNS	1	23-Oct-20	23-Oct-20
C2551	Existing L1 G - FPT for Security System	SMNS	1	29-Oct-20	29-Oct-20
C2552	Existing L1 G - FPT for HVAC	KBA	2	29-Oct-20	30-Oct-20
C2553	Existing L1 G - Clean for Owner/AE Punchlist	HCC	2	29-Oct-20	30-Oct-20
C2554	Existing L1 G - Owner/AE Punchlist	Owner	1	02-Nov-20	02-Nov-20
C2555	Existing L1 G - Electrical Inspector Acceptance for Occupancy	VECA	1	03-Nov-20	03-Nov-20
C2556	Existing L1 G - Mechanical Inspector Acceptance for Occupancy	HP	1	03-Nov-20	03-Nov-20
C2557	Existing L1 G - FPT for Audio Visual	VECA	2	03-Nov-20	04-Nov-20
Phase 2 - Level 2 Renovation			34	21-Sep-20 A	05-Nov-20
Phase 2 - Level 2 Renovation - GL C-E 14-19 (B)			33	21-Sep-20 A	04-Nov-20
C2320	Existing L2 B - Frame / Top Rock Early Walls	AP	4	21-Sep-20 A	24-Sep-20
C2322	Existing L2 B - OH RI Sheetmetal & Plumbing	HP	6	21-Sep-20 A	28-Sep-20
C2428	Existing L2 B - OH RI Steel Sprinkler Pipe	RHFP	6	21-Sep-20 A	28-Sep-20
C2323	Existing L2 B - OH RI Elec / Lights	VECA	7	21-Sep-20 A	29-Sep-20
C2310	Existing L2 B - Demo / Abate / Install Drag Strut GL E-E.5 / 19.6	SK	5	24-Sep-20*	30-Sep-20
C2429	Existing L2 B - Replace Spline Ceiling GL 19.6 Drag Strut	AP	1	01-Oct-20	01-Oct-20
C2326	Existing L2 B - Frame Walls / Set HM Frames	AP	4	02-Oct-20	07-Oct-20
C2327	Existing L2 B - Wall RI Sheetmetal & Plumbing	HP	3	08-Oct-20	12-Oct-20
C2412	Existing L2 B - Wall Elect RI	VECA	3	08-Oct-20	12-Oct-20
C2328	Existing L2 B - Rock Walls / Ceilings	AP	4	13-Oct-20	16-Oct-20
C2330	Existing L2 B - Tape Walls / Ceilings	AP	5	19-Oct-20	23-Oct-20
C2390	Existing L2 B - Pourback Metal Deck Infill at Stairway	SK	2	26-Oct-20*	27-Oct-20
C2410	Existing L2 B - Paint Walls / Ceilings	NWC	4	26-Oct-20	29-Oct-20
C2411	Existing L2 B - Install Plumbing Fixtures	HP	2	30-Oct-20	02-Nov-20
C2332	Existing L2 B - Large Format Tile & Grout	D9	4	30-Oct-20	04-Nov-20
Phase 2 - Level 2 Renovation - Shearwall GL C-C.5 / 5-14 (E)			4	02-Nov-20	05-Nov-20
C2313	Existing L2 E - Layout / Core Drill / Form	IW	4	02-Nov-20	05-Nov-20
Phase 2 - Level 3 Renovation			29	28-Sep-20	05-Nov-20
Phase 2 - Level 3 Renovation - Corridor 3220 GL 2.5-8.5 & Existing Corridor 1245 GL 8.5-9.5			29	28-Sep-20	05-Nov-20
C2731	Existing L3 B - Staff / Furniture Relocations	Owner	5	28-Sep-20*	02-Oct-20
C2734	Existing L3 B - Make Safe Electrical	VECA	1	05-Oct-20	05-Oct-20
C2733	Existing L3 B - Demo Ceiling / Lighting	PAS	2	06-Oct-20	07-Oct-20
C2735	Existing L3 B - Mark Duct For Demo	HP	1	08-Oct-20	08-Oct-20
C2736	Existing L3 B - Mark Electrical For Demo	VECA	1	08-Oct-20	08-Oct-20
C2737	Existing L3 B - Cut / Cap / Demo Duct & Electrical	PAS	2	09-Oct-20	12-Oct-20
C2732	Existing L3 B - Build Pedestrian Access Scaffolding	AP	4	09-Oct-20	14-Oct-20
C2738	Existing L3 B - Demo / Abatement	PAS	12	14-Oct-20	29-Oct-20



Hoffman's most recent 6-week lookahead (09/22/20, continued)

ID	Activity Name	Sub	Dur	Start	Finish
C2739	Existing L3 B - Layout & Overhead Hangers Mechanical	HP	2	28-Oct-20	29-Oct-20
C2740	Existing L3 B - Layout & Overhead Hangers Electrical	VECA	2	28-Oct-20	29-Oct-20
C2741	Existing L3 B - Layout & Overhead Hangers / Rough-In Fire Protection	RHFP	2	28-Oct-20	29-Oct-20
C2752	Existing L3 B - Install Collector Plates	SK	3	29-Oct-20	02-Nov-20
C2742	Existing L3 B - Spray Applied Fireproofing	NORKO	3	03-Nov-20	05-Nov-20
Phase 2 - Level 4 Renovation			40	14-Sep-20 A	06-Nov-20
Phase 2 - Level 4 Renovation - Major Crime Unit & C Line Offices GL 4 -13 (A)			40	14-Sep-20 A	06-Nov-20
C2569	Existing L4 A - Prep for Containment	PAS	10	14-Sep-20 A	25-Sep-20
C2570	Existing L4 A - Abatement at MCU & Offices: Grids C / 4-14	PAS	10	16-Sep-20 A	29-Sep-20
C2586	Existing L4 A - Tear Down Containment	PAS	2	30-Sep-20	01-Oct-20
C2571	Existing L4 A - Layout & Overhead Hangers Mechanical Piping	HP	5	02-Oct-20	08-Oct-20
C2572	Existing L4 A - Layout & Overhead Hangers Mechanical	HP	5	02-Oct-20	08-Oct-20
C2587	Existing L4 A - Install Louvers at West Elevation	KCO	5	02-Oct-20	08-Oct-20
C2573	Existing L4 A - Layout & Overhead Hangers Electrical	VECA	2	07-Oct-20	08-Oct-20
C2574	Existing L4 A - Layout & Overhead Hangers Fire Protection	HP	2	07-Oct-20	08-Oct-20
C2575	Existing L4 A - Install Collector Plates & Beam Bracing (Including Inspecti	SK	5	02-Nov-20*	06-Nov-20
Phase 2 - Trial Courtroom Renovations			194	24-Feb-20 A	24-Nov-20
Phase 2 - Courtroom 2A			4	25-Sep-20	30-Sep-20
C2466	Courtroom 2A - Hand Patch Fireproofing	MULTI	1	25-Sep-20*	25-Sep-20
C2468	Courtroom 2A - Test Plumbing Waste Line	HP	1	28-Sep-20	28-Sep-20
C2469	Courtroom 2A - Replace Spline Ceiling	AP	2	29-Sep-20	30-Sep-20
Phase 2 - Courtroom 3A			177	24-Feb-20 A	30-Oct-20
C2155	Courtroom 3A - Install Audio Visual Equipment		5	24-Feb-20 A	30-Oct-20
C1706	Courtroom 3A - TCO	HCC	0		30-Oct-20
Phase 2 - Courtroom 3E (West)			32	12-Oct-20	24-Nov-20
C2633	Courtroom 3E - Staff / Furniture Relocations	Owner	5	12-Oct-20*	16-Oct-20
C2634	Courtroom 3E - Barricade & Partition Off Remodel Spaces	HSI	2	19-Oct-20	20-Oct-20
C2636	Courtroom 3E - Make Safe Electrical	VECA	2	19-Oct-20	20-Oct-20
C2635	Courtroom 3E - Demo Ceiling & Flooring	PAS	3	20-Oct-20	22-Oct-20
C2637	Courtroom 3E - Mark Duct For Demo	HP	1	23-Oct-20	23-Oct-20
C2658	Courtroom 3E - Mark Electrical For Demo	VECA	1	23-Oct-20	23-Oct-20
C2638	Courtroom 3E - Cut / Cap / Demo Duct & Electrical	PAS	2	26-Oct-20	27-Oct-20
C2639	Courtroom 3E - Demo / Abatement	PAS	20	28-Oct-20	24-Nov-20
Phase 2 - Jury Deliberation Room 3325			19	12-Oct-20	05-Nov-20
C2687	Jury Room 3325 - Staff / Furniture Relocations	Owner	5	12-Oct-20*	16-Oct-20
C2688	Jury Room 3325 - Barricade & Partition Off Remodel Spaces	HSI	1	19-Oct-20	19-Oct-20
C2689	Jury Room 3325 - Remove Spine Ceiling	PAS	2	19-Oct-20	20-Oct-20
C2690	Jury Room 3325 - Make Safe Electrical	VECA	2	19-Oct-20	20-Oct-20
C2691	Jury Room 3325 - Mark Duct For Demo	HP	1	21-Oct-20	21-Oct-20
C2692	Jury Room 3325 - Mark Electrical For Demo	VECA	1	21-Oct-20	21-Oct-20
C2693	Jury Room 3325 - Cut / Cap / Demo Duct & Electrical	PAS	1	22-Oct-20	22-Oct-20
C2694	Jury Room 3325 - Demo / Abatement	PAS	5	23-Oct-20	29-Oct-20
C2695	Jury Room 3325 - Layout & Overhead Hangers Mechanical	HP	1	30-Oct-20	30-Oct-20
C2696	Jury Room 3325 - Layout & Overhead Hangers Electrical	VECA	1	30-Oct-20	30-Oct-20
C2697	Jury Room 3325 - Layout & Overhead Hangers / Rough-In Fire Protection	RHFP	1	02-Nov-20	02-Nov-20
C2698	Jury Room 3325 - Spray Applied Fireproofing	NORKO	3	03-Nov-20	05-Nov-20
Phase 3 - Existing Elevator Renovation			41	09-Sep-20 A	04-Nov-20
Phase 3 - Existing Elevator Renovation - Car 3			18	09-Sep-20 A	02-Oct-20
C2476	Elev Car 3 - Car Side Door Prep And Installation	KONE	7	09-Sep-20 A	25-Sep-20



Hoffman's most recent 6-week lookahead (09/22/20, continued)

ID	Activity Name	Sub	Dur	Start	Finish
C2537	Elev Car 3 - Commissioning / Adjusting	KONE	4	21-Sep-20 A	01-Oct-20
C2477	Elev Car 3 - State Inspection	KONE	1	02-Oct-20	02-Oct-20
C2478	Elev Car 3 - Back In Service	KONE	0		02-Oct-20
Phase 3 - Existing Elevator Renovation - Car 2			24	02-Oct-20	04-Nov-20
C2479	Elev Car 2 - Post Safety Signs	KONE	2	02-Oct-20	05-Oct-20
C2480	Elev Car 2 - Daily JHA And Task Reporting (Job Duration)	KONE	2	06-Oct-20	07-Oct-20
C2481	Elev Car 2 - Site Meeting / GC / Owner/ KONE Installers	KONE	1	08-Oct-20	08-Oct-20
C2482	Elev Car 2 - Mobilize On Site/Protection Of Finishes	KONE	4	09-Oct-20	14-Oct-20
C2483	Elev Car 2 - Demo Machine Room	KONE	4	15-Oct-20	20-Oct-20
C2484	Elev Car 2 - Demo Machine - Partial Hoistway Demo	KONE	4	21-Oct-20	26-Oct-20
C2485	Elev Car 2 - Crane Day - Remove Machine - Hoist Machine	KONE	3	27-Oct-20	29-Oct-20
C2486	Elev Car 2 - Machine Install	KONE	4	30-Oct-20	04-Nov-20
