



Courthouse Project Update Meeting 07.25.19

MT. BAKER CONFERENCE ROOM | ROBERT J. DREWEL BUILDING

MEETING SERIES IS NOW MONTHLY: next instance, 08.22.19

New and/or updated items indicated by bold italics

3000 Rockefeller Ave., M/S 404
Everett, WA 98201-4046
425.388.3087
www.snoco.org

Dave Somers
County Executive

1. Schedule

a. Current Schedule Impacts

- **Winter Storm Impact** – Hoffman has requested a 24-day time extension to the schedule (24 calendar days, 16 working days). The Project Team is now reviewing the additional supporting information requested from Hoffman.

b. Upcoming Activities – see also 5.a-5.b. and 6.b.-6.e.

Continue installing the building curtainwall, continue framing the interior and exterior of the Addition through Level 3, install fire sprinklers in the Addition and future restroom continue building the Addition MEP (mechanical / electrical / plumbing) risers, connecting each floor to the Addition's MEP risers, begin renovations in Courtrooms 2E and 5C, and build out the north side of the restroom core (install tile, fixtures, countertops, and partitions).

c. Progress to Date

Began installing the building curtainwall on the west side of the Addition at Level 1; began installing tile flooring in the Level 1 restrooms, installed countertops in the Level 1 and 2 restrooms, erected steel for the new entrance and upper roof canopies; installed a manlift on the east side of the Addition; applied fireproofing to Addition structural steel through Level 5; erected the Addition mechanical riser between Levels 2 and 5; began framing the exterior of Addition Level 1 and the interior of Levels 1 and 2; began overhead MEP work on Addition Levels 1 to 3; erected Addition structural steel and installed metal floor decking; performed renovations in Courtrooms 2C, 2D, and 5A; installed acoustical ceilings in the Basement renovation areas.

2. Contract Metrics

- Hoffman given Notice To Proceed: 7/30/2018
- Phase 1 Projected Completion: 2/3/20
- Phase 2 Substantial Completion: 2/8/21**
 - Reflects seven-day non-compensable time extension to cover delays resulting from removal of contaminated soils and the remnants of the old County Detention Home.
- Original Project Budget (approved by Council 7/30/2018): \$76,579,770
 - Adjustment due to removal of art allowance: -\$441,417
 - Revised Project Budget: \$76,138,353
- Work Complete and Invoiced Through 5/31/19: \$25,693,733**

3. Changes

4. Upcoming Project Decisions Needing Court Input

Due Date	Item
	<i>None at this time.</i>



5. Stakeholder Concerns

- a. **Minimizing Noise Disruptions** – *In response to stakeholder concerns about noise from steelwork activities, the project's noise mitigation plan has so far been successful. The Project Team will provide advance notice to Superior and District Courts regarding activities which may carry major noise impacts, especially those which must continue in order to maintain schedule.*
- b. **Phase 2 Office Move Planning Meetings** – *The Project Team has begun Phase 2 (2020-21) planning meetings with building stakeholder groups. Our meeting schedule is on Page 4.*

6. Announcements / Action Items

- a. **Update Meeting Series Now Monthly** – *Our next scheduled instances in the series will be August 22, September 19, October 24, November 21, and December 19. We will still distribute a weekly update.*
- b. **Addition Work**
 - i. *The mechanical riser is taking shape on the east side of the addition, with duct currently extending to the middle of Level 5.*
 - ii. *Crews will form the Addition curtain wall, the non-structural outer covering of the building protecting against weather, from west to east around the building.*
- c. **Current and Upcoming Courtroom Work (2019-20)** – *Work in the following courtrooms will include patching ceilings; replacing carpet, HVAC boxes, pews, and jury chairs; and installing sprinkler piping and acoustic fabric panels.*
 - i. **3A (District Court Department 2)** – *ongoing since April 1. Abatement and fireproofing done, sprinklers and HVAC ducts installed, and soffit framing has started. The courtroom will be turned over once the Addition is complete and open.*
 - ii. **2E (Superior Court Department 4)** – *August 17 to September 15.*
 - iii. **2B (Superior Court Department 1)** – *Crews will return to finalize upgrades, December 19 to January 3.*
- d. **Early Phase 2 Courtroom and Chambers Work (2019)** – *Work in these areas includes installation of structural elements, such as drag struts and collector plates.*
 - i. **5C Courtroom and Chambers Area (Superior Court Department 9)** – *ongoing as of July 20, with scheduled completion August 11.*
 - ii. **5D Chambers Area (Superior Court Department 10 & 10.5)** – *October 5 to October 27.*
 - iii. **5A & 5B Chambers Areas (respectively, Depts. 12 & 11)** – *December 23 to January 1.*
- e. **Rosetta Stone (Figure 2)** – *The Project Team uses the table in Figure 2 to align current and new courtroom numbers and the judges assigned to those rooms.*
- f. **Next CBRE Heery Site Visit** – *expected Autumn 2019 after work in Courtrooms 2C, 2D, and 2E has completed.*



MEETING ATTENDANCE

	SUPERIOR COURT		DISTRICT COURT		EXECUTIVE'S OFFICE
X	Judge Bruce Weiss		Judge Anthony Howard		Ken Klein
X	Judge Linda Krese		Judge Tam Bui	X	Josh Dugan
	Judge George Appel	X	Lauren Bjurstrom		
	Judge Millie Judge	X	Lonnie Enyeart		COUNCIL STAFF
	Commissioner Susan Gaer				Geoffrey Thomas
X	Shane Nybo		SHERIFF'S OFFICE	X	Heidi Beazizo
X	Andrew Somers		Ty Trenary		
		X	Jeff Brand		OFFICE for PUBLIC DEFENSE
	CLERK'S OFFICE		Sean Gillespie		Jason Schwarz
	Sonya Kraski				Kristin Crane
X	Mark Allen		PROSECUTING ATTORNEY		
	Shelia Postle		Michael Held		INFORMATION TECHNOLOGY
					JD Braathen
	FACILITIES & FLEET		LAW LIBRARY		Kirk Copple
X	Mark Thunberg		Lettice Parker		
X	Jeff Hencz				OAC SERVICES
X	Steve Slawson		BAR ASSOCIATION		Kevin Fromm
X	Lolly Huggins		Joyce Wood		Glen Lyons



Figure 1: Phase 2 meetings schedule, updated 06.24.19.

DATE	TIME	PMO meets with	PURPOSE / OBJECTIVES OF MEETING
JULY 23	8:00	Superior Court	<ul style="list-style-type: none"> • Present move plan • Identify if adjustments needed • Agree on follow-up
	10:15	15-min. break	
	10:30	District Court	
JULY 30	8:00	Sheriff's Office	<ul style="list-style-type: none"> • Present move plan • Identify if adjustments needed • Agree on follow-up
	10:15	15-min. break	
	10:30	Office for the Public Defense	
AUG 1	8:00	Clerk's Office	<ul style="list-style-type: none"> • Present move plan • Identify if adjustments needed • Agree on follow-up
	8:45	15-min. break	
	9:00	Law Library	
	9:45	15-min. break	
	10:00	Bar Association	
	10:45	15-min. break	
	11:00	Marshals & Transport	
AUG 6	10:30	Prosecuting Attorney	<ul style="list-style-type: none"> • Present move plan • Identify if adjustments needed • Agree on follow-up
AUG 13	10:30	Hoffman	Check-in with construction superintendent.
AUG 15	8:00	HOLD	Hold for follow-up meetings.
AUG 20	10:30	PMO (& others as needed)	Compile and present draft Phase 2 deliverable (move plan) for acceptance.
AUG 27	10:30	PMO (& others as needed)	Adjust draft Phase 2 deliverable (unless initial draft accepted).
AUG 29	8:00	HOLD	Hold for follow-up meetings.
SEPT 3	10:30	PMO (& others as needed)	Adjust draft Phase 2 deliverable (unless initial draft accepted).
SEPT 10	10:30	PMO	Accepted Phase 2 deliverable.

PMO: Courthouse Project Management Office (SnoCo Facilities & Fleet, OAC Services)




Figure 2: Courtroom Rosetta Stone.

COURTROOM DESIGNATIONS BY FLOOR AND BY JUDGE			
NEW	CURRENT	JUDGE	NOTES
5A	Superior Dept 12	Ellis	
5B	Superior Dept 11	Krese	
5C	Superior Dept 9	Farris	
5D	Superior Dept 10	Weiss	<i>current Presiding Judge</i>
4A	NEW	TBD	<i>old Kinard Conference Room</i>
3A	District Dept 2	Bui	
3B	District Dept 3	Howard	
3C	District Dept 1	<i>(District Hearings)</i>	<i>to be relocated from 1 (east side)</i>
3D	N/A	<i>(shell space)</i>	
3E	Superior Dept 7	Wilson	
3F	Superior Dept 8	Lucas	
2A	C201	Okoloko	<i>high-profile trial courtroom</i>
2B	Superior Dept 1	Thompson	<i>Judge Appel at DJJC</i>
2C	Superior Dept 2	Okrent	
2D	Superior Dept 3	Larsen	
2E	Superior Dept 4	Langbehn	<i>Judge Judge at DJJC</i>
1A	C304	<i>(Superior Court Criminal Hearings)</i>	<i>to be relocated from 3 (south side)</i>
NEW	CURRENT	COMMISSIONER	NOTES
1B	Commissioner A	Moriarty	
1C	Commissioner B	Waggoner	
1D	Commissioner C	Gaer	
1E	Commissioner D	Brudvik	

The new courtroom numbering scheme represents the renovation's wayfinding improvements.



Figure 3: Progress Photo.

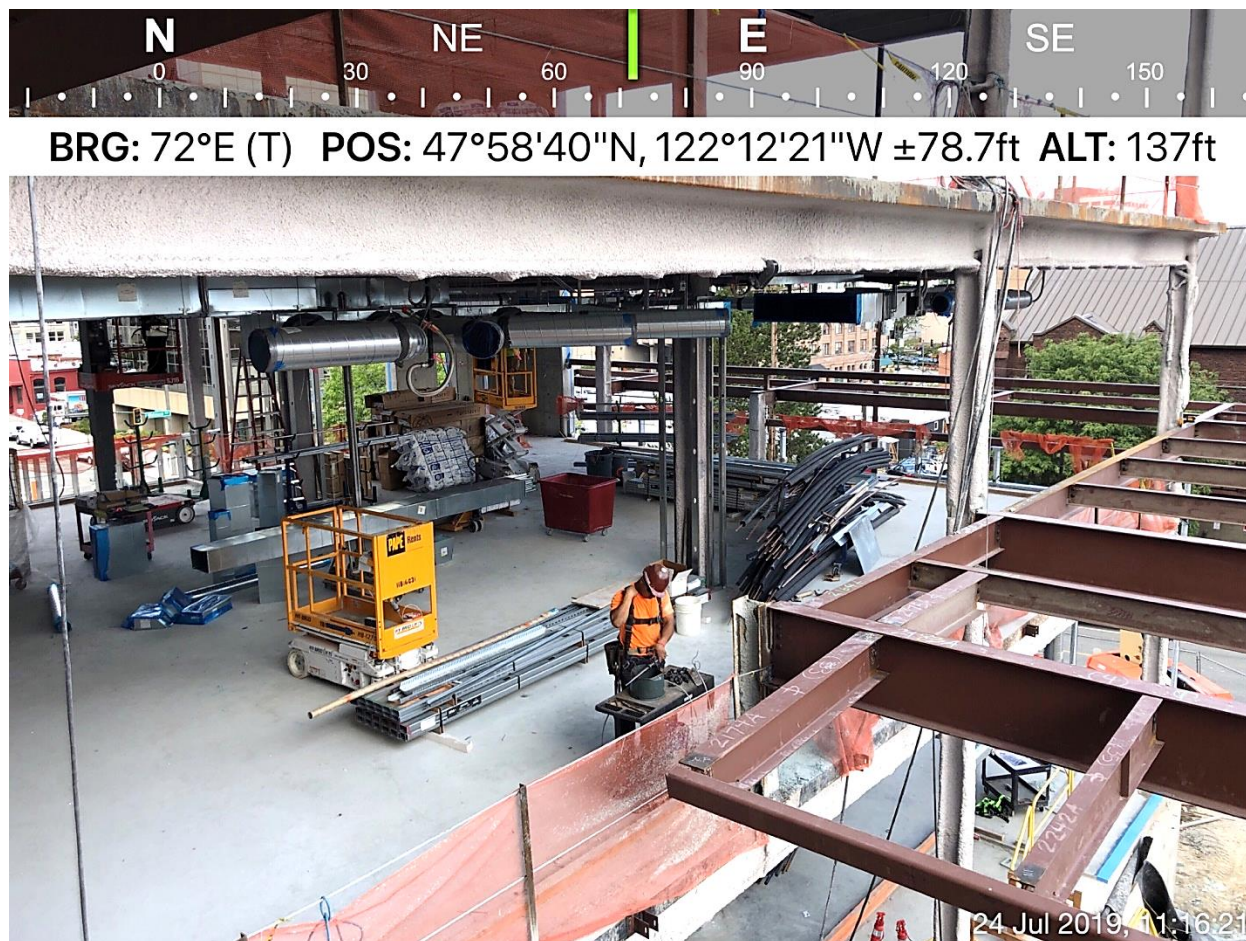

As viewed from the Addition Core stairs, work in progress on Level 2 of the Addition. At right and in center background is the lower canopy. The future Courthouse entrance would be one floor below where the worker in the center of the photo is standing. At center left background, a portion of exterior framing on the west elevation (opposite side) of the Addition can be seen.



Hoffman's most recent 6-week lookahead (7/23/19, first page)

ID	Activity Name	Sub	Dur	Start	Actual Start	Finish
Phase 1 - Addition, Existing Basement Remodel, RR Core				105	25-Apr-19 A	23-Sep-19
Phase 1 - New Addition				105	25-Apr-19 A	23-Sep-19
Phase 1 - North Shearwall				15	25-Apr-19 A	16-Aug-19
C1655	NSW - Repair Finishes at North Shearwall at Basement			15	25-Apr-19 A	16-Aug-19
Phase 1 - New Addition - Foundation & Structure				19	17-Jul-19 A	12-Aug-19
Phase 1 - New Addition - Foundation & Structure - SOG Down				4	07-Aug-19	12-Aug-19
C1071	Addition - Monokote / Fireproof Structure Under Level 1 Deck	IT		4	07-Aug-19	12-Aug-19
Phase 1 - New Addition - Foundation & Structure - Level 1				5	22-Jul-19 A	26-Jul-19
C2054	Addition - Install Secondary Canopy Steel and Decks ***RFI 317 series	SK		5	22-Jul-19 A	26-Jul-19
Phase 1 - New Addition - Foundation & Structure - Level 5				5	17-Jul-19 A	23-Jul-19
C1086	Addition - Monokote / Fireproof Under Roof Deck	IT		5	17-Jul-19 A	23-Jul-19
Phase 1 - New Addition - Foundation & Structure - Roof Level				9	23-Jul-19	02-Aug-19
C2058	Addition - Electrical Sleeves / Inserts at High Roof	VECA		1	23-Jul-19*	23-Jul-19
C2059	Addition - Mechanical Sleeves / Inserts at High Roof	HP		1	23-Jul-19*	23-Jul-19
C2060	Addition - Rebar Deck at High Roof	IW		1	25-Jul-19*	25-Jul-19
C2061	Addition - Pour High Roof Deck	SK		1	26-Jul-19*	26-Jul-19
C2066	Addition - Install Galvanized Mechanical Screenwall Steel at High Roof Deck	SK		4	26-Jul-19*	31-Jul-19
C2063	Addition - Pre Clip for Studs at High Roof Deck	SK		2	29-Jul-19	30-Jul-19
C2064	Addition - Fireproofing at High Roof Deck	IT		3	31-Jul-19	02-Aug-19
Phase 1 - New Addition - Building Envelope				47	18-Jul-19 A	23-Sep-19
C1074	Addition - Ext - Install Roofing Membrane (or Temp Roof - Weather Contr	SDR		20	19-Aug-19	16-Sep-19
Phase 1 - New Addition - Building Envelope - L1 - L2				13	22-Jul-19 A	07-Aug-19
C2015	Addition - Ext (L1 - L2 East / North) - Framing / Sheathing / WAB ***RFI 3	AP		5	22-Jul-19 A	26-Jul-19
C2065	Addition - Ext (L1 - L2 East / North) - Curtainwall	GF		13	22-Jul-19 A	07-Aug-19
Phase 1 - New Addition - Building Envelope - West L2 to Roof				47	18-Jul-19 A	23-Sep-19
C2018	Addition - Ext (L2 - Roof - West) - Framing / Sheathing / WAB ***RFI 197	AP		15	18-Jul-19 A	07-Aug-19
C2020	Addition - Ext (L2 - Roof - West) - Curtainwall	GF		8	08-Aug-19	19-Aug-19
C2042	Addition - Ext - (All Elevations) - Metal Panel Field Measure	KCO		9	20-Aug-19	30-Aug-19
C2027	Addition - Ext (L2 - Roof - West) - UHPC Panels	KCO		13	20-Aug-19	06-Sep-19
C2043	Addition - Ext - (All Elevations) - Metal Panel Lead time	KCO		15	03-Sep-19	23-Sep-19
Phase 1 - New Addition - Building Envelope - North L2 to Roof				24	08-Aug-19	11-Sep-19
C2040	Addition - Ext (L2 - Roof - North) - Framing / Sheathing / WAB	AP		12	08-Aug-19	23-Aug-19
C2041	Addition - Ext (L2 - Roof - North) - Flashing	KCO		4	26-Aug-19	29-Aug-19
C2021	Addition - Ext (L2 - Roof - North) - Curtainwall	GF		8	30-Aug-19	11-Sep-19
Phase 1 - New Addition - Building Envelope - East L2 to Roof				15	26-Aug-19	16-Sep-19
C2022	Addition - Ext (L2 - Roof - East) - Framing / Sheathing / WAB	AP		15	26-Aug-19	16-Sep-19
Phase 1 - New Addition - Interior Buildout & Fit-Up				47	12-Jul-19 A	17-Sep-19
Phase 1 - New Addition - Interior Buildout & Fit-Up - Level 1				12	22-Jul-19 A	06-Aug-19
C1480	Addition L1 - Frame Walls / Soffits / Ceilings	AP		6	22-Jul-19 A	29-Jul-19
C1481	Addition L1 - RI Wall Mechanical	HP		5	30-Jul-19	05-Aug-19
C1482	Addition L1 - RI Wall Electrical	VECA		5	30-Jul-19	05-Aug-19
C1483	Addition L1 - Complete Cover Inspections	HCC		1	06-Aug-19	06-Aug-19
Phase 1 - New Addition - Interior Buildout & Fit-Up - Level 2				21	19-Jul-19 A	16-Aug-19
C1502	Addition L2 - RI Overhead Fire Sprinkler System	HP		5	19-Jul-19 A	25-Jul-19
C1503	Addition L2 - RI Overhead Mechanical	HP		10	22-Jul-19 A	02-Aug-19
C1504	Addition L2 - RI Overhead Electrical	VECA		5	23-Jul-19*	29-Jul-19
C1505	Addition L2 - Frame Walls / Soffits / Ceilings	AP		4	05-Aug-19*	08-Aug-19
C1506	Addition L2 - RI Wall Mechanical	HP		5	09-Aug-19	15-Aug-19



Hoffman's most recent 6-week lookahead (7/23/19, continued)

ID	Activity Name	Sub	Dur	Start	Actual Start	Finish
C1507	Addition L2 - RI Wall Electrical	VECA		5	09-Aug-19	15-Aug-19
C1508	Addition L2 - Complete Cover Inspections	HCC		1	16-Aug-19	16-Aug-19
Phase 1 - New Addition - Interior Buildout & Fit-Up - Level 3				22	26-Jul-19	26-Aug-19
C1527	Addition L3 - RI Overhead Fire Sprinkler System	HP		4	26-Jul-19	31-Jul-19
C1529	Addition L3 - RI Overhead Electrical	VECA		8	30-Jul-19	08-Aug-19
C1528	Addition L3 - RI Overhead Mechanical	HP		10	05-Aug-19*	16-Aug-19
C1530	Addition L3 - Frame / Soffits / Ceilings	AP		6	09-Aug-19	16-Aug-19
C2067	Addition L3 - Frame Walls	AP		4	16-Aug-19	21-Aug-19
C1531	Addition L3 - RI Wall Mechanical	HP		5	19-Aug-19	23-Aug-19
C1532	Addition L3 - RI Wall Electrical	VECA		5	19-Aug-19	23-Aug-19
C1533	Addition L3 - Complete Cover Inspections	HCC		1	26-Aug-19	26-Aug-19
Phase 1 - New Addition - Interior Buildout & Fit-Up - Level 4				29	24-Jul-19	03-Sep-19
C1549	Addition L4 - Interior Buildout Start	HCC		0	24-Jul-19*	
C1608	Addition L4 - MEP Riser Rough-In			4	24-Jul-19*	29-Jul-19
C1551	Addition L4 - Layout Walls	AP		2	26-Jul-19*	29-Jul-19
C1552	Addition L4 - RI Overhead Fire Sprinkler System	HP		4	02-Aug-19	07-Aug-19
C1554	Addition L4 - RI Overhead Electrical	VECA		5	20-Aug-19	26-Aug-19
C1553	Addition L4 - RI Overhead Mechanical	HP		10	20-Aug-19	03-Sep-19
Phase 1 - New Addition - Interior Buildout & Fit-Up - Level 5				26	05-Aug-19	10-Sep-19
C1574	Addition L5 - Interior Buildout Start	HCC		0	05-Aug-19*	
C1576	Addition L5 - Layout Walls	AP		3	05-Aug-19	07-Aug-19
C1577	Addition L5 - RI Overhead Fire Sprinkler System	HP		4	05-Aug-19	08-Aug-19
C1609	Addition L5 - MEP Riser Rough-In			4	05-Aug-19	08-Aug-19
C1579	Addition L5 - RI Overhead Electrical	VECA		5	27-Aug-19	03-Sep-19
C1578	Addition L5 - RI Overhead Mechanical	HP		10	27-Aug-19	10-Sep-19
Phase 1 - New Addition - Interior Buildout & Fit-Up - Elevators & Stairs				47	12-Jul-19 A	17-Sep-19
C1070	Addition Elevator - Install Stairs and Elevator Spreader Beams	SK		20	12-Jul-19 A	08-Aug-19
C2062	Addition Elevator - Procure Green Board for Elevator Shafts	AP		8	01-Aug-19	12-Aug-19
C1082	Addition Elevator - Frame / Rock Elevator & Stair Shaft Enclosures	AP		25	13-Aug-19	17-Sep-19
Phase 1 - Basement Level Renovation				5	16-Aug-19	22-Aug-19
C1752.3	Existing BL - Cut Access Into Existing Building	IW		5	16-Aug-19*	22-Aug-19
Phase 1 - New Restroom Core in Existing Building				34	19-Jul-19 A	05-Sep-19
Phase 1 - New Restroom Core - Level 1				28	23-Jul-19	29-Aug-19
C1366	New RR L1 - Install Flooring & Base	D9		5	23-Jul-19*	29-Jul-19
C1362	New RR L1 - Install Wall Tile	D9		5	30-Jul-19	05-Aug-19
C1363	New RR L1 - Trim Out Mechanical	HP		3	06-Aug-19	08-Aug-19
C1364	New RR L1 - Trim Out Electrical	VECA		3	06-Aug-19	08-Aug-19
C1365	New RR L1 - Trim Out Fire Sprinklers	HP		3	06-Aug-19	08-Aug-19
C1368	New RR L1 - Install Toilets / Fixtures / Accessories	BD		5	09-Aug-19	15-Aug-19
C1369	New RR L1 - Install Partitions	AP		5	16-Aug-19	22-Aug-19
C1367	New RR L1 - Install Countertops	ART		3	23-Aug-19	27-Aug-19
C1359	New RR L1 - Install Doors & Hardware	BHW		2	28-Aug-19	29-Aug-19
C1373	New RR L1 - Construction Complete	HCC		0		29-Aug-19
Phase 1 - New Restroom Core - Level 2				32	19-Jul-19 A	03-Sep-19
C1386	New RR L2 - Paint	NWC		4	19-Jul-19 A	24-Jul-19
C1391	New RR L2 - Install Flooring & Base	D9		5	25-Jul-19	31-Jul-19
C1387	New RR L2 - Install Wall Tile	D9		5	01-Aug-19	07-Aug-19
C1388	New RR L2 - Trim Out Mechanical	HP		3	08-Aug-19	12-Aug-19



Snohomish County

Facilities Management

Courthouse Project

Hoffman's most recent 6-week lookahead (7/23/19, continued)

ID	Activity Name	Sub	Dur	Start	Actual Start	Finish
C1389	New RR L2 - Trim Out Electrical	VECA		3	08-Aug-19	12-Aug-19
C1390	New RR L2 - Trim Out Fire Sprinklers	HP		3	08-Aug-19	12-Aug-19
C1393	New RR L2 - Install Toilets / Fixtures / Accessories	BD		5	13-Aug-19	19-Aug-19
C1394	New RR L2 - Install Partitions	AP		5	20-Aug-19	26-Aug-19
C1392	New RR L2 - Install Countertops	ART		3	27-Aug-19	29-Aug-19
C1384	New RR L2 - Install Doors & Hardware	BHW		2	30-Aug-19	03-Sep-19
Phase 1 - New Restroom Core - Level 3				30	23-Jul-19	03-Sep-19
C1941	New RR L3 - Tape & Finish GWB	AP		3	23-Jul-19*	25-Jul-19
C1411	New RR L3 - Paint	NWC		4	26-Jul-19	31-Jul-19
C1416	New RR L3 - Install Flooring & Base	D9		5	01-Aug-19	07-Aug-19
C1412	New RR L3 - Install Wall Tile	D9		5	08-Aug-19	14-Aug-19
C1413	New RR L3 - Trim Out Mechanical	HP		3	15-Aug-19	19-Aug-19
C1414	New RR L3 - Trim Out Electrical	VECA		3	15-Aug-19	19-Aug-19
C1415	New RR L3 - Trim Out Fire Sprinklers	HP		3	15-Aug-19	19-Aug-19
C1418	New RR L3 - Install Toilets / Fixtures / Accessories	BD		5	20-Aug-19	26-Aug-19
C1419	New RR L3 - Install Partitions	AP		5	27-Aug-19	03-Sep-19
Phase 1 - New Restroom Core - Level 4				31	22-Jul-19 A	03-Sep-19
C1435	New RR L4 - Install Hard Lid Ceiling	AP		4	22-Jul-19 A	25-Jul-19
C1433	New RR L4 - Hang GWB Walls	AP		5	23-Jul-19*	29-Jul-19
C1948	New RR L4 - Tape & Finish GWB	AP		3	30-Jul-19	01-Aug-19
C1436	New RR L4 - Paint	NWC		4	02-Aug-19	07-Aug-19
C1441	New RR L4 - Install Flooring & Base	D9		5	08-Aug-19	14-Aug-19
C1437	New RR L4 - Install Wall Tile	D9		5	15-Aug-19	21-Aug-19
C1438	New RR L4 - Trim Out Mechanical	HP		3	22-Aug-19	26-Aug-19
C1439	New RR L4 - Trim Out Electrical	VECA		3	22-Aug-19	26-Aug-19
C1440	New RR L4 - Trim Out Fire Sprinklers	HP		3	22-Aug-19	26-Aug-19
C1443	New RR L4 - Install Toilets / Fixtures / Accessories	BD		5	27-Aug-19	03-Sep-19
Phase 1 - New Restroom Core - Level 5				33	22-Jul-19 A	05-Sep-19
C1997	New RR L5 - Frame Ceilings @ F-Line (Including MEP Finishes)	AP		3	22-Jul-19 A	24-Jul-19
C1457	New RR L5 - Complete Cover Inspections	HCC		1	25-Jul-19	25-Jul-19
C1460	New RR L5 - Install Hard Lid Ceiling	AP		4	26-Jul-19	31-Jul-19
C1458	New RR L5 - Hang GWB Walls	AP		5	30-Jul-19	05-Aug-19
C1955	New RR L5 - Tape & Finish GWB	AP		3	01-Aug-19	05-Aug-19
C1461	New RR L5 - Paint	NWC		4	06-Aug-19	09-Aug-19
C1466	New RR L5 - Install Flooring & Base	D9		5	12-Aug-19	16-Aug-19
C1462	New RR L5 - Install Wall Tile	D9		5	19-Aug-19	23-Aug-19
C1463	New RR L5 - Trim Out Mechanical	HP		3	26-Aug-19	28-Aug-19
C1464	New RR L5 - Trim Out Electrical	VECA		3	26-Aug-19	28-Aug-19
C1465	New RR L5 - Trim Out Fire Sprinklers	HP		3	26-Aug-19	28-Aug-19
C1468	New RR L5 - Install Toilets / Fixtures / Accessories	BD		5	29-Aug-19	05-Sep-19
Phase 2 - Existing Courthouse Renovation				68	17-Jun-19 A	20-Sep-19
Phase 2 - South Shearwall				5	17-Jun-19 A	16-Aug-19
C1984	SSW - FRP Shearwall Footing	IW		5	17-Jun-19 A	16-Aug-19
Phase 2 - Trial Courtroom Renovations				66	19-Jun-19 A	20-Sep-19
Phase 2 - Courtroom 2E				13	19-Aug-19	05-Sep-19
C1687	Courtroom 2E - Demo / Abate	PAS		1	19-Aug-19*	19-Aug-19
C1730	Courtroom 2E - Fire Proofing	IT		3	20-Aug-19	22-Aug-19



Hoffman's most recent 6-week lookahead (7/23/19, continued)

ID	Activity Name	Sub	Dur	Start	Actual Start	Finish
C1688	Courtroom 2E - Replace Mechanical Boxes	HP		4	21-Aug-19	26-Aug-19
C1689	Courtroom 2E - Re-Term Electrical	VECA		3	23-Aug-19	27-Aug-19
C1690	Courtroom 2E - Complete Cover Inspections	HCC		0		27-Aug-19
C1691	Courtroom 2E - Re-Install Ceiling	AP		3	28-Aug-19	30-Aug-19
C1692	Courtroom 2E - Install Flooring & Base	D9		5	29-Aug-19	05-Sep-19
Phase 2 - Courtroom 3A				46	19-Jun-19 A	22-Aug-19
C1699	Courtroom 3A - RI Overhead Electrical	VECA		5	19-Jun-19 A	31-Jul-19
C1701	Courtroom 3A - Install Soffit / Ceiling / Fixtures	AP		10	24-Jul-19*	06-Aug-19
C1698	Courtroom 3A - RI Overhead Mechanical	HP		5	25-Jul-19*	31-Jul-19
C1700	Courtroom 3A - Complete Cover Inspections	HCC		0		31-Jul-19
C1702	Courtroom 3A - Install Flooring & Base	D9		5	07-Aug-19	13-Aug-19
C1703	Courtroom 3A - Re-Install Courtroom Furniture	HCC		5	14-Aug-19	20-Aug-19
C1704	Courtroom 3A - Final Clean & Punchlist	HCC		1	21-Aug-19	21-Aug-19
C1705	Courtroom 3A - Punchlist Corrections	HCC		1	22-Aug-19	22-Aug-19
C1706	Courtroom 3A - TCO	HCC		0		22-Aug-19
Phase 2 - Courtroom 3C				20	23-Aug-19	20-Sep-19
C1707	Courtroom 3C - Demo / Abate	PAS		20	23-Aug-19	20-Sep-19
Phase 2 - Courtroom 5C				14	19-Jul-19 A	07-Aug-19
C2046	Courtroom 5C - Demo / Abate	HP		6	19-Jul-19 A	24-Jul-19
C2050	Courtroom 5C - Remove Ductwork	PAS		2	23-Jul-19	24-Jul-19
C2047	Courtroom 5C - Install Drag Strut	SK		10	25-Jul-19	07-Aug-19
